Project Methodolgy CA - Lofthus Frukt og Saft

19.mai.2019

http://

Prosjektleder	Stian Helgeland
Prosjekt start/slutt datoer	20.mai.2019 - 29.jun.2019
Avsluttet	0%
Oppgave	20
Deltakere	4

Gantt Chart for a new website project for the company called "Lofthus Frukt og Saft".

Oppgave

Navn	Startdato	Sluttdato
Meet with client *Meet with the client to get an overview of what they have and what they need.*	20.05.19	20.05.19
Choose other professional disciplines *After the meeting, go through the notes from the meeting to get a bigger picture of what other professional disciplines need to complete this project.*	21.05.19	21.05.19
Meet with inhouse / consulting personnel.	21.05.19	21.05.19
Research competitors. *Research competitors.*	20.05.19	21.05.19
Brainstorming with the team *Brainstorm ideas together as a team.*	21.05.19	22.05.19
Sketches / Wireframes *Start sketching and wireframing possible designs.*	23.05.19	28.05.19
Copywriter write content *Copywriter start to write content for the website.*	29.05.19	07.06.19
Photographer on location *Send photographer to the client's location to gather image content. As a result of the brainstorming session, there will be a list of required pictures to be used within the design of the website.*	23.05.19	24.05.19
Edit photographs *Edit the photographs taken on location.*	27.05.19	28.05.19
Inform client of progress *Inform client of progress so far.*	03.06.19	03.06.19
Show client design concepts. *Show client the design concepts and wireframes.*	03.06.19	03.06.19
Update wireframes based on feedback *Update wireframes according to feedback from client.*	04.06.19	04.06.19
Code Mockup *Code a mock-up of the different pages within the website.*	05.06.19	05.06.19
Get finished images *Get edited images from the photographer.*	06.06.19	06.06.19
Website coding *Coding of the website.*	10.06.19	21.06.19
Finishing touches *Finishing touches on the website.*	24.06.19	25.06.19

Oppgave

Navn	Startdato	Sluttdato
Testing *Testing of all the elements of the website*	10.06.19	25.06.19
Upload website to client's domain *Upload the website to client's domain.*	25.06.19	25.06.19
Finalize testing	26.06.19	27.06.19
Deliver product to client *Meet with clients to deliver the finished product.*	28.06.19	28.06.19

Deltakere

Navn	Standardrolle
Stian Helgeland	Prosjektleder
Person Numbertwo	Photographer
Person Numberthree	Copywriter
Person Numberfour	Front-end Developer

Ganttskjema

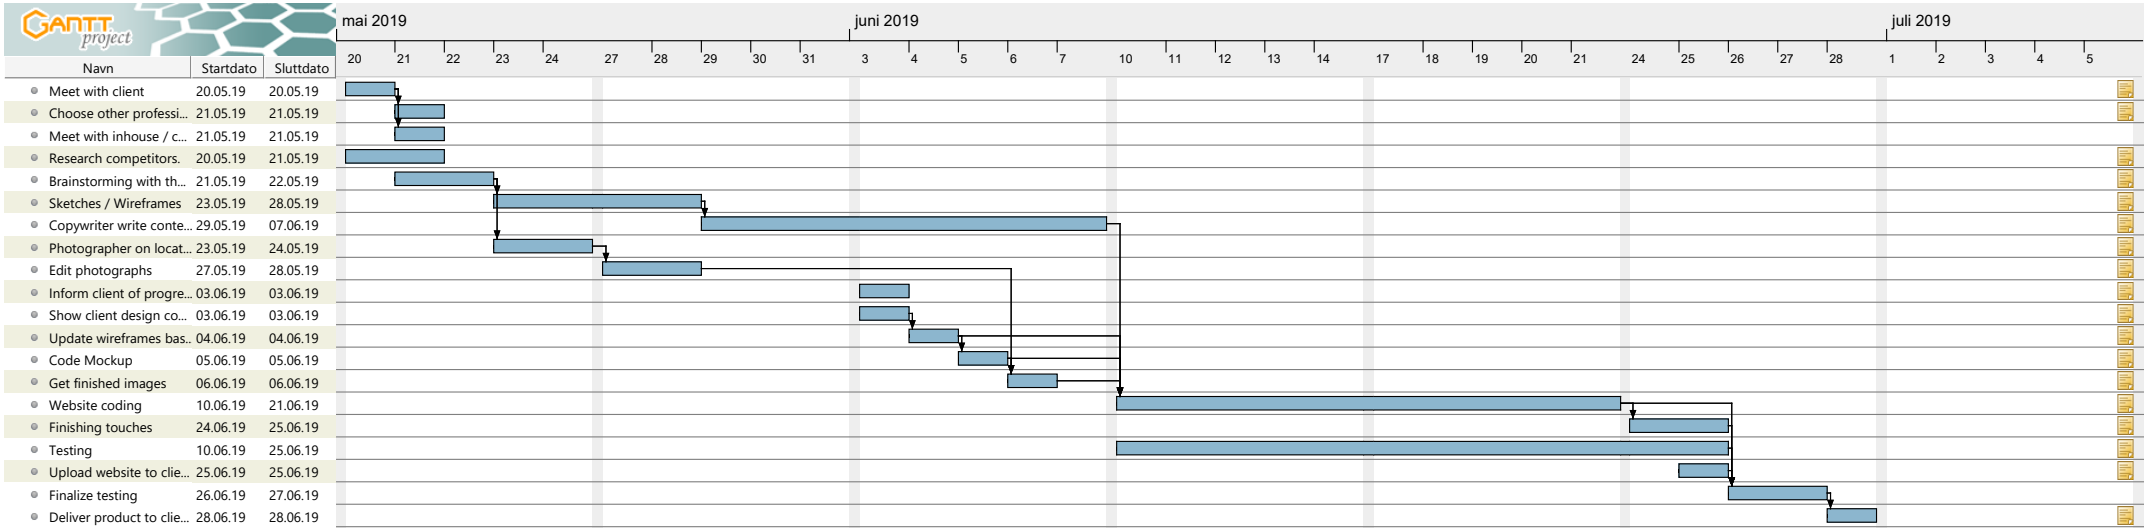

Navn	Startdato	Sluttdato
Meet with client	20.05.19	20.05.19
Choose other professi...	21.05.19	21.05.19
Meet with inhouse / c...	21.05.19	21.05.19
Research competitors.	20.05.19	21.05.19
Brainstorming with th...	21.05.19	22.05.19
Sketches / Wireframes	23.05.19	28.05.19
Copywriter write conte...	29.05.19	07.06.19
Photographer on locat...	23.05.19	24.05.19
Edit photographs	27.05.19	28.05.19
Inform client of progre...	03.06.19	03.06.19
Show client design co...	03.06.19	03.06.19
Update wireframes bas..	04.06.19	04.06.19
Code Mockup	05.06.19	05.06.19
Get finished images	06.06.19	06.06.19
Website coding	10.06.19	21.06.19
Finishing touches	24.06.19	25.06.19
Testing	10.06.19	25.06.19
Upload website to clie...	25.06.19	25.06.19
Finalize testing	26.06.19	27.06.19
Deliver product to clie...	28.06.19	28.06.19

Personelloversikt
